City of Clear Lake Shores, Texas East Parking Lot Task # 3

NL Concrete Services LLC

Project Start Date: 10/11/2024 (Friday)
Project Lead: Francisco Guerra
Display Week: 2
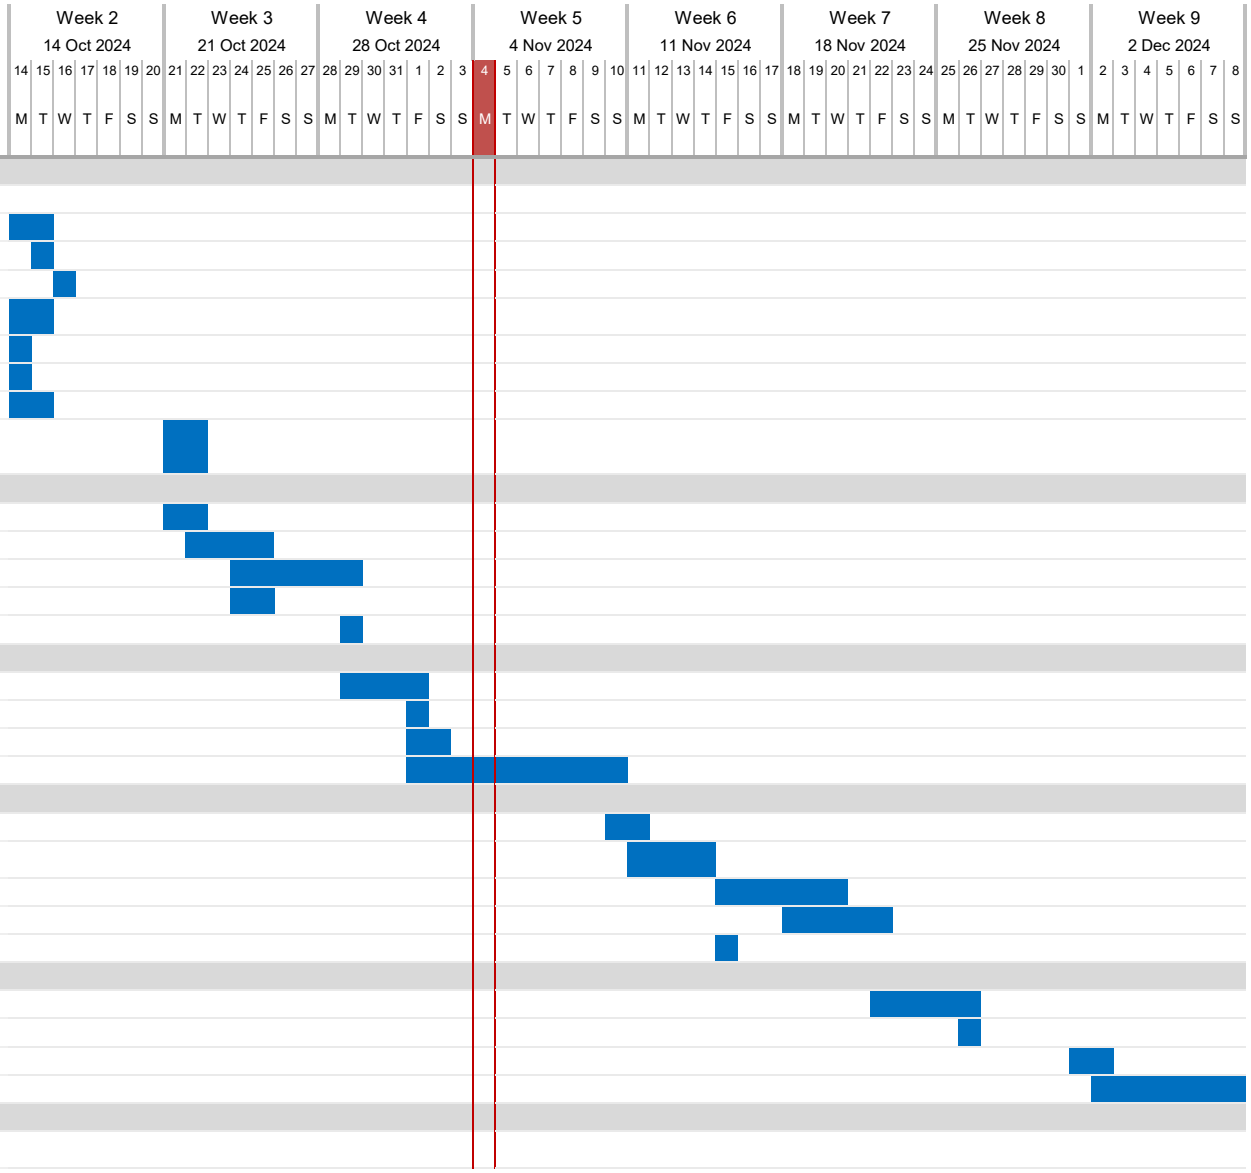
WBS	TASK	LEAD	START	END	DAYS	% DONE	WORK DAYS
1	**Planning**			-			-
1.1	Notice of Award		Thu 10/03/24	Sat 10/12/24	10	100%	7
1.2	Contracting		Sat 10/12/24	Tue 10/15/24	4	60%	2
1.3	Pre-Construction kickoff		Tue 10/15/24	Tue 10/15/24	1	0%	1
1.4	Notice to Proceed		Wed 10/16/24	Wed 10/16/24	1	75%	1
1.4.1	Permitting (811, Sawcut, Mobility)		Fri 10/11/24	Tue 10/15/24	5	50%	3
1.4.2	Submittals		Fri 10/11/24	Mon 10/14/24	4	50%	2
1.5	Pre-Construction photos		Mon 10/14/24	Mon 10/14/24	1	0%	1
1.6	Schedule of Values		Mon 10/14/24	Tue 10/15/24	2	0%	2
1.7	Mobilization /Equipment, signage, traffic control, SWPP		Mon 10/21/24	Tue 10/22/24	2	0%	2
2	**Phase I Demolition**			-			-
2.1	Surveying and staking		Mon 10/21/24	Tue 10/22/24	2	0%	2
2.2	Demo and Excavating		Tue 10/22/24	Fri 10/25/24	4	0%	4
2.3	Lime Stabilization		Thu 10/24/24	Tue 10/29/24	6	0%	4
2.31	Light Pole relocation x 2		Thu 10/24/24	Fri 10/25/24	5	0%	5
2.32	Inspection		Tue 10/29/24	Tue 10/29/24	1	0%	1
3	**Phase I Forming & Finishing**			-			-
3.1	Form setting		Tue 10/29/24	Fri 11/01/24	4	0%	4
3.2	Inspection		Fri 11/01/24	Fri 11/01/24	1	0%	1
3.3	Concrete Placement		Fri 11/01/24	Sat 11/02/24	2	0%	1
3.4	Curing		Fri 11/01/24	Sun 11/10/24	10	0%	6
4	**Phase II Demolition**			-			-
4.1	Surveying and staking		Sun 11/10/24	Mon 11/11/24	2	0%	1
4.2	Demo and Excavating with lighting relocation		Mon 11/11/24	Thu 11/14/24	4	0%	4
4.3	Lime Stabilization		Fri 11/15/24	Wed 11/20/24	6	0%	4
4.311	Light Pole relocation x 2		Mon 11/18/24	Fri 11/22/24	5	0%	5
4.312	Inspection		Fri 11/15/24	Fri 11/15/24	1	0%	1
5	**Phase II Forming & Finishing**			-			-
5.1	Form setting		Fri 11/22/24	Tue 11/26/24	5	0%	3
5.2	Inspection		Tue 11/26/24	Tue 11/26/24	1	0%	1
5.3	Concrete Placement		Sun 12/01/24	Mon 12/02/24	2	0%	1
5.4	Curing & Restoration		Mon 12/02/24	Wed 12/11/24	10	0%	8
6	**Phase 1 & 2 Landscaping and Striping**			-			-
6.1	Power wash Phase I and stripe		Thu 12/12/24	Fri 12/13/24	2	0%	2
